

Variable	Mean	SD	Min	Max
Age	34.2	10.5	20	55
Gender	Male	Female		
Marital status	Married	Single		
Education	High school	College		
Occupation	Manager	Worker		
Income	Low	High		
Health status	Good	Poor		
Smoking status	Smoker	Non-smoker		
Alcohol consumption	Regular	Occasional		
Exercise frequency	Regular	Occasional		
Stress level	Low	High		
Sleep quality	Good	Poor		
Dietary habits	Healthy	Unhealthy		
Family size	Small	Large		
Work-life balance	Good	Poor		
Life satisfaction	High	Low		
Overall well-being	Good	Poor		

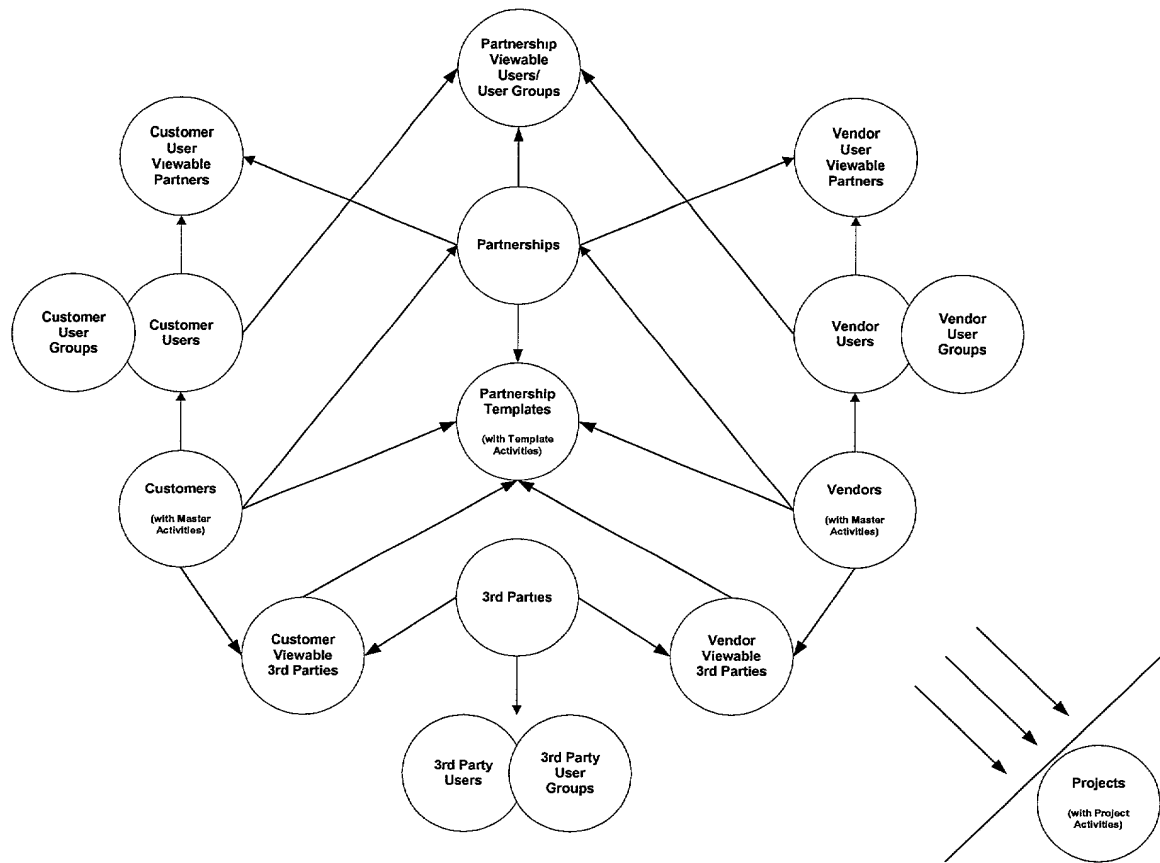


FIGURE 1

0966710-092801
FOI260-0129550




Company Profile	
<div>SubmitCancel</div>	
Name:	ABC Packaging Company
Division:	Display Division
Workdays:	<input type="checkbox"/> Sun <input checked="" type="checkbox"/> Mon <input checked="" type="checkbox"/> Tue <input checked="" type="checkbox"/> Wed <input checked="" type="checkbox"/> Thu <input checked="" type="checkbox"/> Fri <input type="checkbox"/> Sat
Non-Working Dates:	<div><div></div><div>12/24/2001, 12/25/2001</div><div></div></div> <div></div>

FIGURE 2

Activities	Workdays
Seq	Activity Name
1	Cost & Feasibility Form Initiated
2	Brand Approvals
3	Submit Design Development Request to Vendors
4	Structure Submitted to Customer
5	Structure Approved
6	Die-Lines Submitted to Art Agency
7	Art Submitted to Customer by Agency
8	Art Approved
9	Specs Submitted for Pricing
10	Pricing Submitted to Customer
11	Pricing Approved
12	Purchase Order Issued
13	Product Ordered
14	Work Order Submitted to Manufacturing
15	Cutting Dies Ordered
16	Printing Plates Ordered
17	Outside Parts Purchased
18	All Proofs Approved
19	Component Manufacturing Start
20	Component Manufacturing Finish
21	Components Received at Assembly
22	Product Received at Assembly
23	Assembly Start

FIGURE 2A

108260-0129660

Activity Table More Fields							
Activities		Workdays					
Seq	Working Days						
1	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
2	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
3	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
4	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
5	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
6	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
7	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
8	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
9	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
10	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
11	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
12	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
13	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
14	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
15	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
16	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
17	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
18	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
19	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
20	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
21	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
22	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat
23	<input type="checkbox"/> Sun	<input checked="" type="checkbox"/> Mon	<input checked="" type="checkbox"/> Tue	<input checked="" type="checkbox"/> Wed	<input checked="" type="checkbox"/> Thu	<input checked="" type="checkbox"/> Fri	<input type="checkbox"/> Sat

FIGURE 2B

09966710-09301
T08260-01/99660

Activity Table More Fields			
Category Fields			
Label1:	Account	Value1:	WalMart KMart CVS Eckerd
Label2:	Style	Value2:	Floorstand Sidekick
Label3:		Value3:	
Label4:		Value4:	
Label5:		Value5:	
Label6:		Value6:	
Label7:		Value7:	
Label8:		Value8:	
Label9:		Value9:	
Label10:		Value10:	
Customer Fields			
Label1:	Purchase Order Number		
Label2:	PO Quantity		
Label3:	Brand		
Label4:			
Label5:			
Label6:			
Label7:			
Label8:			
Label9:			
Label10:			
Label11:			
Label12:			
Label13:			
Label14:			
Label15:			

FIGURE 2C

Cross Reference Setup Parameters	
Continue	Cancel
Choose a Vendor and Customer for this relationship:	
Vendor:	<input type="text"/>
Customer/Div:	<input type="text"/>
Template Name:	<input type="text"/>

FIGURE 3

Activity Table More Fields			
#	Responsible Company	Customer Activity	Vendor Activity
	<input type="text" value="Customer"/>	<input type="text"/>	<input type="text"/>
	Add	Insert	Delete
1	Customer	Cost & Feasibility Form Initiated	Cost & Feasibility Form Initiated
2	Customer	Brand Approvals	Brand Approvals
3	Customer	Submit Design Development Request to Ve	Submit Design Development Request to Ve
4	Vendor	Structure Submitted to Customer	Structure Submitted to Customer
5	Customer	Structure Approved	Structure Approved
6	Vendor	Die-Lines Submitted to Art Agency	Die-Lines Submitted to Art Agency
7	Customer	Art Submitted to Customer by Agency	Art Submitted to Customer by Agency
8	Customer	Art Approved	Art Approved
9	Vendor	Specs Submitted for Pricing	Specs Submitted for Pricing
10	Vendor	Pricing Submitted to Customer	Pricing Submitted to Customer
11	Customer	Pricing Approved	Pricing Approved
12	Customer	Purchase Order Issued	Purchase Order Issued
13	Customer	Product Ordered	Product Ordered
14	Vendor	Work Order Submitted to Manufacturing	Work Order Submitted to Manufacturing
15	Vendor	Cutting Dies Ordered	Cutting Dies Ordered
16	Vendor	Printing Plates Ordered	Printing Plates Ordered
17	Vendor	Outside Parts Purchased	Outside Parts Purchased
18	Customer	All Proofs Approved	All Proofs Approved
19	Vendor	Component Manufacturing Start	Component Manufacturing Start
20	Vendor	Component Manufacturing Finish	Component Manufacturing Finish

FIGURE 4

FOI b6 b7C b7D

Relationship Template : New Product Promotion		
<input type="button" value="Submit"/> <input type="button" value="Cancel"/>		
<input checked="" type="checkbox"/>	Enabled	
Name:	Home Products, Inc.	Vendor Information
Division:	Consumer Division	ABC Packaging Company
Project Contact:	<input type="text" value="James Grissom"/>	Display Division
		<input type="text" value="Nick Cornaglia"/>
Notification Users:	<div><input checked="" type="checkbox"/> James Grissom</div> <div><input type="checkbox"/> Kathy Cline</div> <div><input type="checkbox"/> Larry Shutzberg</div>	<div><input type="checkbox"/> Becca Spann</div> <div><input type="checkbox"/> Jack Ratcliff</div> <div><input checked="" type="checkbox"/> Nick Cornaglia</div>
Maintenance Users:	<div><input type="checkbox"/> James Grissom</div> <div><input checked="" type="checkbox"/> Kathy Cline</div> <div><input checked="" type="checkbox"/> Larry Shutzberg</div> <div><input type="checkbox"/> BUYERS</div>	<div><input type="checkbox"/> Becca Spann</div> <div><input checked="" type="checkbox"/> Jack Ratcliff</div> <div><input type="checkbox"/> Nick Cornaglia</div> <div><input checked="" type="checkbox"/> DESIGNERS</div>
Pending Attachments:	<div><input type="text"/></div> <div><input type="button" value="Add Attachment"/></div>	

FIGURE 5

Project Info
More Info

Customer Info

Account:
Style:
Purchase Order Number:
PO Quantity:
Brand:

Vendor Info

Design Number:
Manufactured Quantity:
Assembled Quantity:
QA Released Quantity:
Shipped Quantity:

FIGURE 5A

Activity Table More Fields					
Activities Workdays		Responsible Company	Responsible User	Seq	+Days
1	Cost & Feasibility Form Initiated	Customer	James Grissom		
2	Brand Approvals	Customer	James Grissom	1	2
3	Submit Design Development Request to Vendors	Customer	Kathy Cline	2	1
4	Structure Submitted to Customer	Vendor	Jack Ratcliff	3	5
5	Structure Approved	Customer	Kathy Cline	4	2
6	Die-Lines Submitted to Art Agency	Vendor	Jack Ratcliff	5	2
7	Art Submitted to Customer by Agency	Customer	Larry Shutzberg	6	5
8	Art Approved	Customer	Larry Shutzberg	7	2
9	Specs Submitted for Pricing	Vendor	Jack Ratcliff	8	2
10	Pricing Submitted to Customer	Vendor	Nick Cornaglia	9	2
11	Pricing Approved	Customer	James Grissom	10	1
12	Purchase Order Issued	Customer	Kathy Cline	11	2
13	Product Ordered	Customer	Kathy Cline	12	1
14	Work Order Submitted to Manufacturing	Vendor	Jack Ratcliff	12	1
15	Cutting Dies Ordered	Vendor	Nick Cornaglia	14	2
16	Printing Plates Ordered	Vendor	Nick Cornaglia	14	2
17	Outside Parts Purchased	Vendor	Jack Ratcliff	14	2

FIGURE 5B

FIGURE 5C

0966710-096601

Name: Adv. Notification: Notification Users:	Customer Information Home Products, Inc.	Vendor Information ABC Packaging Company
	Days	Days
	<input checked="" type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input checked="" type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia
	Maintenance Users:	
	<input type="checkbox"/> James Grissom <input checked="" type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg <input type="checkbox"/> BUYERS	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input checked="" type="checkbox"/> Nick Cornaglia <input type="checkbox"/> DESIGNERS
<input type="button" value="OK"/> <input type="button" value="Cancel"/>		

FIGURE 5D

Project Creation - Select Partner & Template	
<input type="button" value="Continue"/>	<input type="button" value="Cancel"/>
Customer:	<input type="text" value="Home Products"/>
Template:	<input type="text" value="New Product Promotion"/>

FIGURE 6

Project Creation - Project Info	
<input type="button" value="Continue"/>	<input type="button" value="Cancel"/>
BlueCuda #:	Will be automatically generated
Project Name:	<input type="text"/> <input style="float: right;" type="button" value="Notify NOW!"/>
Name:	Customer Information Home Products, Inc.
Division:	Consumer Division
Project Contact:	<input type="text" value="James Grissom"/>
Item Number:	
Project Status:	Open

FIGURE 7

09966740-099660

Project Info | More Info

Product Information:

Notes / Agreements:

Pending Attachments:

Add Attachment

Notification Users:

Customer Information

☒ James Grissom

☐ Kathy Cline

☐ Larry Shutzberg

Vendor Information

☐ Becca Spann

☐ Jack Ratcliff

☒ Nick Cornaglia

Maintenance Users:

☐ James Grissom

☒ Kathy Cline

☒ Larry Shutzberg

☐ BUYERS

☐ Becca Spann

☒ Jack Ratcliff

☐ Nick Cornaglia

☒ DESIGNERS

FIGURE 7A

Project Info		More Info	
Customer Info			
Account:			
Style:			
Purchase Order Number:			
PO Quantity:			
Brand:			
Vendor Info			
Design Number:			
Manufactured Quantity:			
Assembled Quantity:			
QA Released Quantity:			
Shipped Quantity:			

FIGURE 7B

Activity Information		Dates	Workdays														
Seq	Activity Name	Responsible User	Status	Planned	Actual	Completion Date	Seq	Orig	New	Plan	+Days						
1	Cost & Feasibility Form Initiated	James Grissom	Cpl	08/16/2001	08/16/2001												
2	Brand Approvals	James Grissom	Hld	08/20/2001			1	2		2							
3	Submit Design Development Request to Vendors	Kathy Cline	Opn	08/21/2001			2	1		1							
4	Structure Submitted to Customer	Jack Ratcliff	Opn	08/28/2001			3	5		5							
5	Structure Approved	Kathy Cline	Opn	08/30/2001			4	2		2							
6	Die-Lines Submitted to Art Agency		Can														
7	Art Submitted to Customer by Agency		Can														
8	Art Approved	Larry Shutzberg	Opn	09/03/2001			5	2		2							
9	Specs Submitted for Pricing	Jack Ratcliff	Opn	09/05/2001			8	2		2							
10	Pricing Submitted to Customer	Nick Cornaglia	Opn	09/07/2001			9	2		2							
11	Pricing Approved	James Grissom	Opn	09/10/2001			10	1		1							
12	Purchase Order Issued	Kathy Cline	Opn	09/12/2001			11	2		2							
13	Product Ordered	Kathy Cline	Opn	09/13/2001			12	1		1							
14	Work Order Submitted to Manufacturing	Jack Ratcliff	Opn	09/13/2001			12	1		1							
15	Cutting Dies Ordered	Nick Cornaglia	Opn	09/17/2001			14	2		2							
16	Printing Plates Ordered	Nick Cornaglia	Opn	09/17/2001			14	2		2							
17	Outside Parts Purchased	Jack Ratcliff	Opn	09/17/2001			14	2		2							
18	All Proofs Approved	James Grissom	Opn	09/26/2001			16	7		7							

FIGURE 8

09966710-092801
T08260-01/99660

Project Creation - More Activity Info		
<div>Return</div> <div>Cancel</div>		
BlueCuda #:	43	
Project Name:	Lemon Cough Drop Display	
Activity Sequence:	1	
Activity Name:	Cost & Feasibility Form Initiated	
Name:	Customer Information	Vendor Information
Adv. Notification:	Home Products, Inc.	ABC Packaging Company
Notification Users:	<div>1 Days</div> <div><input checked="" type="checkbox"/> James Grissom</div> <div><input type="checkbox"/> Kathy Cline</div> <div><input type="checkbox"/> Larry Shutzberg</div>	<div>1 Days</div> <div><input type="checkbox"/> Becca Spann</div> <div><input checked="" type="checkbox"/> Jack Ratcliff</div> <div><input type="checkbox"/> Nick Cornaglia</div>
Maintenance Users:	<div><input type="checkbox"/> James Grissom</div> <div><input checked="" type="checkbox"/> Kathy Cline</div> <div><input type="checkbox"/> Larry Shutzberg</div> <div><input type="checkbox"/> BUYERS</div>	<div><input type="checkbox"/> Becca Spann</div> <div><input type="checkbox"/> Jack Ratcliff</div> <div><input checked="" type="checkbox"/> Nick Cornaglia</div> <div><input type="checkbox"/> DESIGNERS</div>

FIGURE 9



FIGURE 10

0966710.092801

	Customer	Vendor
Accept Close Delete	To: <input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia
	cc: <input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia
	bcc: <input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia
Subject: Project Mgmt. Change Link		
Note: Email will be sent when the Project is submitted.		
<div></div>		

FIGURE 11

Add Activity (1 of 2)	
Continue Cancel	
BlueCuda #:	43
Project Name:	Lemon Cough Drop Display
Activity Name:	<input type="text"/>
Activity Owner:	<input type="text" value="Vendor"/>
Activity Type:	<input type="text" value="Shared"/>
<u>Insert Position</u>	
Before Activity:	<input type="text"/>
After Activity:	<input type="text"/>

FIGURE 12

Add Activity (2 of 2)		
Accept Cancel		
BlueCuda #:	43	
Project Name:	Lemon Cough Drop Display	
Activity Name:	Pricing Quote Approved	
Activity Owner:	Vendor	
Activity Type:	Shared	
Responsible User:	<input type="text"/>	
Work Days:	<input type="checkbox"/> Sun <input checked="" type="checkbox"/> Mon <input checked="" type="checkbox"/> Tue <input checked="" type="checkbox"/> Wed <input checked="" type="checkbox"/> Thu <input checked="" type="checkbox"/> Fri <input type="checkbox"/> Sat	
Notes/Agreements:	<input type="text"/>	
Name:	Customer Information	Vendor Information
Adv. Notification:	Home Products, Inc.	ABC Packaging Company
Notification Users:	<input type="text" value="Days"/> <input checked="" type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg	<input type="text" value="Days"/> <input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input checked="" type="checkbox"/> Nick Cornaglia
Maintenance Users:	<input type="text"/> <input type="checkbox"/> James Grissom <input type="checkbox"/> Kathy Cline <input type="checkbox"/> Larry Shutzberg <input type="checkbox"/> BUYERS	<input type="text"/> <input type="checkbox"/> Becca Spann <input type="checkbox"/> Jack Ratcliff <input type="checkbox"/> Nick Cornaglia <input type="checkbox"/> DESIGNERS

FIGURE 12A

09966710-099660

Structure Submitted to Customer		
Submit	Cancel	
BlueCuda #:	49	
Project Name:	Back to School Promo	
	<input checked="" type="checkbox"/> Notify NOW!	
	Customer Information	Vendor Information
Name:	Home Products, Inc.	ABC Packaging Company
Division:	Consumer Division	Display Division
Project Contact:	Larry Shutzberg	Nick Cornaglia
Responsible User: ●	Jack Ratcliff	
Third Party:		
Activity Status:	Open	
Workdays:	Mon, Tue, Wed, Thu, Fri	
	Planned	Actual
Completion Date:	07/11/2001	<input type="checkbox"/> Today <input type="checkbox"/> Yesterday
Notes/Agreements:		
Pending Attachments:		<input type="button" value="Add Attachment"/>

FIGURE 13

- ▶ My Projects
 - Project
 - Plan Date
 - Activity

FIGURE 14





















My Projects		Grouping: Ungrouped			Show: Late		
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Update Selected Activities							
Activity		Responsibility		Planned		Actual	
	... Cherry Fizzy Antacid SK - 45 (Home Products) 						
	Structure Approved	Kathy Cline	Opn	8/28/01	<input type="text"/>		 
	... Lemon Cough Drop Display - 43 (Home Products) 						
	Brand Approvals	James Grissom	Hld	8/20/01	<input type="text"/>		 
	Submit Design Development Request to Vendors	Kathy Cline	Opn	8/21/01	<input type="text"/>		 
	Structure Submitted to Customer	Jack Ratcliff	Opn	8/28/01	<input type="text"/>		 

FIGURE 14A

My Projects by Plan Date		Grouping: Ungrouped			Show: All		
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Update Selected Activities							
Project	Activity	Partner	Responsibility	Planned	Actual		
08/2001							
Cherry Fizzy Antacid SK - 45	Cost & Feasibility Form Initiated	Home Products	James Grissom	Cpl	8/15/01	08/16/2001	Y T
Lemon Cough Drop Display - 43	Cost & Feasibility Form Initiated	Home Products	James Grissom	Cpl	8/16/01	08/16/2001	Y T
Cherry Fizzy Antacid SK - 45	Brand Approvals	Home Products	James Grissom	Cpl	8/17/01	08/16/2001	Y T
Lemon Cough Drop Display - 43	Brand Approvals	Home Products	James Grissom	Hld	8/20/01		Y T

FIGURE 14B

My Projects by Activity		Grouping: Ungrouped			Show: Open	
New Project		Expand	Collapse	Previous	Next	Top GoTo
Update Selected Activities						
Project		Activity	Partner	Responsibility	Planned	Actual
All Proofs Approved						
Lemon Cough Drop Display - 43	All Proofs Approved	Home Products	James Grissom	Opn	9/26/01	<div></div> Y T
Art Approved						
Lemon Cough Drop Display - 43	Art Approved	Home Products	Larry Shutzberg	Opn	9/03/01	<div></div> Y T
Cherry Fizzy Antacid SK - 45	Art Approved	Home Products	Larry Shutzberg	Opn	9/10/01	<div></div> Y T
Art Submitted to Customer by Agency						
Cherry Fizzy Antacid SK - 45	Art Submitted to Customer by Agency	Home Products	Larry Shutzberg	Opn	9/06/01	<div></div> Y T
Assembly Finish						
Lemon Cough Drop Display - 43	Assembly Finish	Home Products	Jack Ratcliff	Opn	10/15/01	<div></div> Y T
Cherry Fizzy Antacid SK - 45	Assembly Finish	Home Products	Jack Ratcliff	Opn	10/22/01	<div></div> Y T
Assembly Start						
Lemon Cough Drop Display - 43	Assembly Start	Home Products	Nick Cornaglia	Opn	10/08/01	<div></div> Y T
Cherry Fizzy Antacid SK - 45	Assembly Start	Home Products	Nick Cornaglia	Opn	10/15/01	<div></div> Y T
Component Manufacturing Finish						
Lemon Cough Drop Display - 43	Component Manufacturing Finish	Home Products	Jack Ratcliff	Opn	10/04/01	<div></div> Y T

FIGURE 14C



FIGURE 15

My Activities by Project				Grouping: Ungrouped		Show: Late	
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Update Selected Activities							
Activity		Responsibility		Planned		Actual	
...	20523823FS Summer Cold Caps 50 - 48 (Home Products)			Opn	8/24/01		
	Structure Submitted to Customer	Jack Ratcliff					
..	2546925SK Spring Allergy Tabs - 47 (Home Products)			Opn	8/15/01		
	Structure Submitted to Customer	Jack Ratcliff					
	Die-Lines Submitted to Art Agency	Jack Ratcliff		Opn	8/21/01		
...	a test - 081701 - 52 (Home Products)			Opn	8/29/01		
	Structure Submitted to Customer	Jack Ratcliff					

FIGURE 15A

My Activities by Plan Date				Grouping: Ungrouped		Show: Open	
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Update Selected Activities							
Project	Activity	Partner	Responsibility	Planned	Actual		
07/2001							
Back to School Promo - 49	Structure Submitted to Customer	Home Products	Jack Ratcliff	Opn	7/11/01		
Back to School Promo - 49	Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn	7/17/01		
Back to School Promo - 49	Specs Submitted for Pricing	Home Products	Jack Ratcliff	Opn	7/30/01		
08/2001							
Winter Flu Tablets 64 - 44	Specs Submitted for Pricing	Home Products	Jack Ratcliff	Opn	8/06/01		
Back to School Promo - 49	Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Opn	8/07/01		

FIGURE 15B

My Activities by Activity Grouping: Ungrouped Show: Late

New Project Expand Collapse Previous Next Top GoTo

Update Selected Activities

Project	Activity	Partner	Responsibility	Planned	Actual
Component Manufacturing Finish					
Back to School Promo - 49	Component Manufacturing Finish	Home Products	Jack Ratcliff	Opn 8/28/01	<input type="text"/> Y T
Die-Lines Submitted to Art Agency					
Back to School Promo - 49	Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn 7/17/01	<input type="text"/> Y T
2546925SK Spring Allergy Tabs - 47	Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn 8/21/01	<input type="text"/> Y T
Outside Parts Purchased					
Back to School Promo - 49	Outside Parts Purchased	Home Products	Jack Ratcliff	Opn 8/09/01	<input type="text"/> Y T
Winter Flu Tablets 64 - 44	Outside Parts Purchased	Home Products	Jack Ratcliff	Opn 8/16/01	<input type="text"/> Y T
Holiday Lipgloss Display - 53	Outside Parts Purchased	Home Products	Jack Ratcliff	Opn 8/23/01	<input type="text"/> Y T

FIGURE 15C

- Company Views**
- Project
 - ▶ Plan Date
 - Activity
 - Responsibility
 - ▶ Activity
 - Plan Date
 - Responsibility
 - ▶ Responsibility
 - Plan Date
 - Activity
 - 3rd Party

FIGURE 16

0966710-09301

Projects		Grouping: Ungrouped		Show: Late			
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Activity		Responsibility		Planned		Actual	
...	25469255K Spring Allergy Tabs - 47 (Home Products)						
	Structure Submitted to Customer	Jack Ratcliff	Opn	8/15/01	---		
...	Back to School Promo - 49 (Home Products)						
	Cost & Feasibility Form Initiated	James Grissom	Opn	7/01/01	---		
	Brand Approvals	James Grissom	Opn	7/03/01	---		
	Submit Design Development Request to Vendors	Kathy Cline	Opn	7/04/01	---		
	Structure Submitted to Customer	Jack Ratcliff	Opn	7/11/01	---		
	Structure Approved	Kathy Cline	Opn	7/13/01	---		
	Die-Lines Submitted to Art Agency	Jack Ratcliff	Opn	7/17/01	---		
	Art Submitted to Customer by Agency	Larry Shutzberg	Opn	7/24/01	---		
	Art Approved	Larry Shutzberg	Opn	7/26/01	---		
	Specs Submitted for Pricing	Jack Ratcliff	Opn	7/30/01	---		
	Pricing Submitted to Customer	Nick Cornaglia	Opn	8/01/01	---		
	Pricing Approved	James Grissom	Opn	8/02/01	---		
	Purchase Order Issued	Kathy Cline	Opn	8/06/01	---		
	Product Ordered	Kathy Cline	Opn	8/07/01	---		
	Work Order Submitted to Manufacturing	Jack Ratcliff	Opn	8/07/01	---		
	Cutting Dies Ordered	Nick Cornaglia	Opn	8/09/01	---		
	Printing Plates Ordered	Nick Cornaglia	Opn	8/09/01	---		
	Outside Parts Purchased	Jack Ratcliff	Opn	8/09/01	---		
...	Headache Gel Caps 24 - 50 (Home Products)						
	Cost & Feasibility Form Initiated	James Grissom	Opn	8/16/01	---		
	Brand Approvals	James Grissom	Opn	8/20/01	---		
	Submit Design Development Request to Vendors	Kathy Cline	Opn	8/21/01	---		
...	Headache Gel Caps 24 - 51 (Home Products)						
	Cost & Feasibility Form Initiated	James Grissom	Opn	8/16/01	---		

FIGURE 16A

Activities by Date/Activity		Grouping: <div>Ungrouped</div>		Show: <div>Open</div>		
New Project	Expand	Collapse	Previous	Next	Top	GoTo
Project	Activity	Partner	Responsibility	Planned	Actual	
07/2001						
Art Approved						
Back to School Promo - 49	Art Approved	Home Products	Larry Shutzberg	Opn	7/26/01	---
Art Submitted to Customer by Agency						
Back to School Promo - 49	Art Submitted to Customer by Agency	Home Products	Larry Shutzberg	Opn	7/24/01	---
Brand Approvals						
Back to School Promo - 49	Brand Approvals	Home Products	James Grissom	Opn	7/03/01	---
Cost & Feasibility Form Initiated						
Back to School Promo - 49	Cost & Feasibility Form Initiated	Home Products	James Grissom	Opn	7/01/01	---
Die-Lines Submitted to Art Agency						
Back to School Promo - 49	Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn	7/17/01	---
Specs Submitted for Pricing						
Back to School Promo - 49	Specs Submitted for Pricing	Home Products	Jack Ratcliff	Opn	7/30/01	---
Structure Approved						
Back to School Promo - 49	Structure Approved	Home Products	Kathy Cline	Opn	7/13/01	---
Winter Flu Tablets 64 - 44	Structure Approved	Home Products	Kathy Cline	Opn	7/20/01	---

FIGURE 16B











Activities by Activity/Date				Grouping: Ungrouped		Show: Open	
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Project		Activity		Partner	Responsibility	Planned	Actual
<div><div></div>All Proofs Approved</div>							
<div><div><div>08/2001</div></div></div>							
Back to School Promo - 49 		● All Proofs Approved		Home Products	James Grissom	Opn	8/20/01 ---
Winter Flu Tablets 64 - 44 		● All Proofs Approved		Home Products	James Grissom	Opn	8/27/01 ---
<div><div><div>09/2001</div></div></div>							
Holiday Lipgloss Display - 53 		● All Proofs Approved		Home Products	James Grissom	Opn	9/03/01 ---
Lemon Cough Drop Display - 43 		● All Proofs Approved		Home Products	James Grissom	Opn	9/26/01 ---
<div><div><div>10/2001</div></div></div>							
20523823FS Summer Cold Caps 50 - 48 		● All Proofs Approved		Home Products	James Grissom	Opn	10/03/01 ---
Headache Gel Caps 24 - 50 		● All Proofs Approved		Home Products	James Grissom	Opn	10/03/01 ---
Wal-Mart Candy Display - 42 		● All Proofs Approved		Home Products	James Grissom	Opn	10/04/01 ---
Summer Sunscreen Promo - 46 		● All Proofs Approved		Home Products	James Grissom	Opn	10/04/01 ---
a test - 081701 - 52 		● All Proofs Approved		Home Products	James Grissom	Opn	10/08/01 ---
<div><div><div>---</div></div></div>							
Headache Gel Caps 24 - 51 		● All Proofs Approved		Home Products	James Grissom	Opn	--- ---

FIGURE 16D

0956710-092801
FOR 260-0749660

Activities by Activity/User				Grouping: Ungrouped		Show: Late	
New Project		Expand	Collapse	Previous	Next	Top	GoTo
Project		Activity		Partner	Responsibility	Planned	Actual
Art Approved							
Larry Shutzberg							
Back to School Promo - 49		Art Approved		Home Products	Larry Shutzberg	Opn	7/26/01 ---
Winter Flu Tablets 64 - 44		Art Approved		Home Products	Larry Shutzberg	Opn	8/02/01 ---
Art Submitted to Customer by Agency							
Larry Shutzberg							
Back to School Promo - 49		Art Submitted to Customer by Agency		Home Products	Larry Shutzberg	Opn	7/24/01 ---
Brand Approvals							
James Grissom							
Back to School Promo - 49		Brand Approvals		Home Products	James Grissom	Opn	7/03/01 ---
20523823FS Summer Cold Caps 50 - 48		Brand Approvals		Home Products	James Grissom	Opn	8/16/01 ---
Lemon Cough Drop Display - 43		Brand Approvals		Home Products	James Grissom	Hld	8/20/01 ---
Headache Gel Caps 24 - 50		Brand Approvals		Home Products	James Grissom	Opn	8/20/01 ---
Cost & Feasibility Form Initiated							
James Grissom							
Back to School Promo - 49		Cost & Feasibility Form Initiated		Home Products	James Grissom	Opn	7/01/01 ---
Wal-Mart Candy Display - 42		Cost & Feasibility Form Initiated		Home Products	James Grissom	Opn	8/15/01 ---

FIGURE 16E

0956710-092801

Activities by User/Date			Grouping: Ungrouped		Show: Completed	
New Project	Expand	Collapse	Previous	Next	Top	GoTo
Project		Activity	Partner	Responsibility	Planned	Actual
Jack Ratcliff						
07/2001						
Winter Flu Tablets 64 - 44		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/18/01 7/18/01
Winter Flu Tablets 64 - 44		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/24/01 7/24/01
Holiday Lipgloss Display - 53		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/25/01 7/25/01
Holiday Lipgloss Display - 53		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/31/01 7/31/01
08/2001						
Holiday Lipgloss Display - 53		Specs Submitted for Pricing	Home Products	Jack Ratcliff	Cpl	8/13/01 8/13/01
Holiday Lipgloss Display - 53		Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Cpl	8/21/01 8/21/01
Cherry Fizzy Antacid SK - 45		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	8/24/01 8/16/01
James Grissom						
07/2001						
Winter Flu Tablets 64 - 44		Cost & Feasibility Form Initiated	Home Products	James Grissom	Cpl	7/06/01 8/10/01
Winter Flu Tablets 64 - 44		Brand Approvals	Home Products	James Grissom	Cpl	7/10/01 8/10/01
Holiday Lipgloss Display - 53		Cost & Feasibility Form Initiated	Home Products	James Grissom	Cpl	7/13/01 7/13/01
Holiday Lipgloss Display - 53		Brand Approvals	Home Products	James Grissom	Cpl	7/17/01 7/17/01

FIGURE 16F

0956710-092604

Activities by User/Activity			Grouping: Ungrouped		Show: Completed		
New Project	Expand	Collapse	Previous	Next	Top	GoTo	
Project		Activity		Partner	Responsibility	Planned	Actual
Jack Ratcliff							
Die-Lines Submitted to Art Agency							
Winter Flu Tablets 64 - 44		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/24/01	7/24/01
Holiday Lipgloss Display - 53		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Cpl	7/31/01	7/31/01
Specs Submitted for Pricing							
Holiday Lipgloss Display - 53		Specs Submitted for Pricing	Home Products	Jack Ratcliff	Cpl	8/13/01	8/13/01
Structure Submitted to Customer							
Winter Flu Tablets 64 - 44		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/18/01	7/18/01
Holiday Lipgloss Display - 53		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	7/25/01	7/25/01
Cherry Fizzy Antacid SK - 45		Structure Submitted to Customer	Home Products	Jack Ratcliff	Cpl	8/24/01	8/16/01
Work Order Submitted to Manufacturing							
Holiday Lipgloss Display - 53		Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Cpl	8/21/01	8/21/01
James Grissom							
All Proofs Approved							
2546925SK Spring Allergy Tabs - 47		All Proofs Approved	Home Products	James Grissom	Cpl	9/24/01	8/17/01
Brand Approvals							
Winter Flu Tablets 64 - 44		Brand Approvals	Home Products	James Grissom	Cpl	7/10/01	8/10/01
Holiday Lipgloss Display - 53		Brand Approvals	Home Products	James Grissom	Cpl	7/17/01	7/17/01

FIGURE 16G

Activities by 3rd Party							
New Project	Expand	Collapse	Previous	Next	Top	GoTo	
Project	Activity		Partner	Responsibility		Planned	Actual
ABC, Inc.							
Back to School Promo - 49		Die-Lines Submitted to Art Agency	Home Products	Jack Ratcliff	Opn	7/17/01	---
Wal-Mart Candy Display - 42		Work Order Submitted to Manufacturing	Home Products	Jack Ratcliff	Opn	9/21/01	---
Arolston Inc.							
Winter Flu Tablets 64 - 44		Component Manufacturing Finish	Home Products	Jack Ratcliff	Opn	9/04/01	---

FIGURE 16H

Grouping:	Ungrouped
apse	Pre--Select One--
Respo	Ungrouped
	Customer

FIGURE 17

Show:	Open
To:	--Select One--
Plan	All
	All w/o Can
	Held
6/01	Late
	Open
5 (P&G)	Open/Held
9/04	Completed
8/31	Canceled

FIGURE 18

1. Build your search
Fill out **at least one** of the following fields

Search Now
Clear Entries

Document Types
☒ Project ☐ Activity
Project Name

Activity Name

Planned Completion Date
From:
To:
Company Name

Word(s)

Project Contact

Activity Responsible User

Actual Completion Date
From:
To:
Division

All words
BlueCuda #

2. Optional: Refine your search
Fill out **one or more** of the following fields

Search Now
Clear Entries

Max Nbr of docs: Nbr per page: Sort by:

☐ Use word variants & fuzzy search

Use word variants
Also find variations on your words. For example, a search for create will also find creates, creating, created, and creator.

Use fuzzy search
Find similar words or phrases. Even finds misspelled words. For example, a search for pakaging will also find packaging.

FIGURE 19

09966710-092801

BlueCuda Newsletter for Ishutzberg

MY :	Late Activities	Advance Notification	New	Orphaned	Other Changes
Other :	Late Activities	Advance Notification	New	Orphaned	Other Changes

MY LATE ACTIVITIES

Project: [Winter Flu Tablets 64 \(44\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/02/2001

Project: [Back to School Promo \(49\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 07/26/2001

[Return to top](#)

MY ADVANCE NOTIFICATIONS

Project: [Lemon Cough Drop Display \(43\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 09/03/2001

Project: [2546925SK Spring Allergy Tabs \(47\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Submitted to Customer by Agency \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/28/2001

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/30/2001

[Return to top](#)

MY NEW PROJECTS AND ACTIVITIES

Project: [Winter Flu Tablets 64 \(44\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/02/2001

Project: [2546925SK Spring Allergy Tabs \(47\)](#) **Vendor:** ABC Packaging Company

Activity: [Art Submitted to Customer by Agency \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/28/2001

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 08/30/2001

[Return to top](#)

MY ORPHANED ACTIVITIES

Nothing to Report

[Return to top](#)

MY CHANGED PROJECTS AND ACTIVITIES

Project: [Cherry Fizzy Antacid SK \(45\)](#) **Customer:** Home Products, Inc. / Consumer Division

Activity: [Art Approved \(Open\)](#) **Resp:** Larry Shutzberg (Cust) **Due:** 09/10/2001

Added Attachments :

Production Memo.doc on 8/16/01 10:45:19 AM - Larry Shutzberg

FIGURE 20

09966710-092801
T08260-01799660

OTHER LATE ACTIVITIES

Project: Summer Sunscreen Promo (46) **Vendor:** ABC Packaging Company

Activity: Submit Design Development Request to Vendors (Open) **Resp:** Kathy Cline (Cust) **Due:** 08/20/2001

Project: Back to School Promo (49) **Vendor:** ABC Packaging Company

Activity: Submit Design Development Request to Vendors (Open) **Resp:** Kathy Cline (Cust) **Due:** 07/04/2001

[Return to top](#)

OTHER ADVANCE NOTIFICATIONS

Nothing to Report

[Return to top](#)

OTHER NEW PROJECTS AND ACTIVITIES

Nothing to Report

[Return to top](#)

OTHER ORPHANED ACTIVITIES

Nothing to Report

[Return to top](#)

OTHER CHANGED PROJECTS AND ACTIVITIES

Project: 2546925SK Spring Allergy Tabs (47) **Customer:** Home Products, Inc. / Consumer Division

Activity: Submit Design Development Request to Vendors (Completed) **Resp:** Kathy Cline (Cust)

Due: 08/08/2001

Activity Status Change :

Activity Status Open to Completed on 8/16/01 11:00:40 AM - Larry Shutzberg

Actual Completion Date Change :

Actual Completion date 8/8/01 8/16/01 11:00:40 AM - Larry Shutzberg

Added Attachments :

Production Memo.doc on 8/16/01 11:00:40 AM - Larry Shutzberg

Other Changes :

The activity was changed 8/16/01 11:00:40 AM - Larry Shutzberg

[Return to top](#)

FIGURE 20A

BlueCuda Web Reporting

This may take several minutes depending on the number of projects available.

Please select one of the following customers

then select one of the following reports

Click <OK> to continue or <Cancel> to return to previous view.

OK

Cancel

FIGURE 21

BlueCuda Report Selection -- Web Page Dialog

BlueCuda Reporting: Selection Criteria

Preview Cancel

Select items to include on report --

Select All Unselect All

Project Types (Ignore)

(All Assumed)

Select All Unselect All

[blank] Custom Forecasted Promotional

Project Status (Ignore)

(All Assumed)

Select All Unselect All

Open Held Canceled Completed

Business Units (Ignore)

(All Assumed)

Select All Unselect All

[blank] Analgesics GI-Topicals Nutritionals

Brands (Ignore)

Component Vendors (Ignore)

(All Assumed)

Select All Unselect All

[blank] Alliance Altwell Blauvelt

Assembly Vendors (Ignore)

(All Assumed)

Select All Unselect All

[blank] Alliance Altwell Blauvelt

Accounts (Ignore)

(All Assumed)

Select All Unselect All

[blank] Albertson's BJs C-Stores

Sort By --

- BlueCuda #
- Customer Item #
- Component Production Start Date
- Assembly Start Date
- Ship to AHP DCs Date
- Ship to Account DCs Date
- Arrive at Account DCs Date

(the dates above are planned dates)

Include --

- ☒ Product Info
- ☐ Notes / Agreements

FIGURE 21A

09966710-092801

BlueCuda™			ABC Consumer Products Company																		As of 8/6/10 3:01 PM All dates shown as planned over actual									
			Production Scheduling																											
Sorted by: Active in Account DCA Planned Date																														
<div>Order #Project NameStyleAccountForecasted QuantityAssembly VendorComponent VendorPO QuantityComponents Mfg QuantityAssembly QuantityOA Released QuantityShipped QuantitySchedule Production in ASSchedule Assembly PackoutProduct Order #Component Production StartComponent Production FinishComponent Arrival at AssemblyProduct Arrival at AssemblyAssembly StartAssembly FinishFinal OA ReleaseShip to AMP MCAShip to Account DCAStatus</div>																														
457	8/2/10 10/10/10 10/10/10	PDQ	KMA	TD	AM	3,700						7/28	8/14	8/21	8/30	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
847164	8/2/10 10/10/10 10/10/10	PDQ	KMA	AM	AM	3,000						8/27	8/13	8/20	8/28	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
454	8/2/10 10/10/10 10/10/10	PDQ	KMA	AM	AM	3,000						8/22	8/13	8/20	8/28	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
847164	8/2/10 10/10/10 10/10/10	PDQ	KMA	TD	AM	3,700						8/15	8/10	8/17	8/25	8/28	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
456	8/2/10 10/10/10 10/10/10	PDQ	KMA	TD	AM	3,700						8/15	8/10	8/17	8/25	8/28	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
223887	8/2/10 10/10/10 10/10/10	PDQ	KMA	TD	AM	3,700						8/15	8/10	8/17	8/25	8/28	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
465	8/2/10 10/10/10 10/10/10	PDQ	KMA	AM	AM	3,000						8/24	8/10	8/20	8/28	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
847164	8/2/10 10/10/10 10/10/10	PDQ	KMA	AM	AM	3,000						8/24	8/10	8/20	8/28	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	8/31	Open	
453	8/2/10 10/10/10 10/10/10	FS/CK	WLC	AM	AM	4,000						8/24	8/27	8/24	8/14	8/17	8/23	8/26	8/29	8/30	8/30	8/30	8/30	8/30	8/30	8/30	8/30	8/30	Open	
847164	8/2/10 10/10/10 10/10/10	FS/CK	WLC	AM	AM	4,000						8/24	8/27	8/24	8/14	8/17	8/23	8/26	8/29	8/30	8/30	8/30	8/30	8/30	8/30	8/30	8/30	8/30	Open	
Projects selected 5 of 5																														

Projects selected 5 of 5

FIGURE 21B

09966710-092801

ACTIVITY STATUSES	BUSINESS RULES
Open	<ul style="list-style-type: none"> • Automatically defaulted to Open for newly created project activities. • Automatically set to Open when "Release" option is selected on a Held project activity or "Uncancel" option is selected on a Canceled project activity. • Automatically set to Open when ACTUAL COMPLETION DATE is removed from a project activity. • Automatically set to Open for all viewable Held project activities when "Release All" is selected. • Automatically set to Open for all viewable Canceled project activities when "Uncancel All" is selected. "Uncancel All" only affects Canceled project activities.
Held	<ul style="list-style-type: none"> • Automatically set to Held when "Hold" option is selected on an Open or Canceled project activity. Only an Open or Canceled project activity can become Held. • Automatically set to Held for all viewable Open project activities when "Hold All" is selected. "Hold All" only affects Open project activities.
Canceled	<ul style="list-style-type: none"> • Automatically set to Canceled when "Cancel" option is selected on an Open or Held project activity. Only an Open or Held project activity can become Canceled. • Automatically set to Canceled for all viewable Open project activities when "Cancel All" is selected. "Cancel All" only affects Open project activities.
Completed	<ul style="list-style-type: none"> • Automatically set to Completed when ACTUAL COMPLETION DATE is entered on a project activity.

FIGURE 22

09966710-09966710

PROJECT STATUSES	BUSINESS RULES
Open	<ul style="list-style-type: none"> Automatically set to Open if at least one viewable project activity is Open. Other viewable project activities can be Open, Held, Canceled, or Completed.
Held	<ul style="list-style-type: none"> Automatically set to Held if no viewable project activities are Open and at least one viewable project activity is Held. Other viewable project activities can be Held, Canceled, or Completed.
Canceled	<ul style="list-style-type: none"> Automatically set to Canceled if all viewable project activities are either Canceled or Completed and the last viewable project activity is Canceled.
Completed	<ul style="list-style-type: none"> Automatically set to Completed if all viewable project activities are either Canceled or Completed and the last viewable project activity is Completed.

FIGURE 23

USER TYPE	USER CHARACTERISTICS
Customer Lead User (w/ Administration)	User defined for a Customer with LEAD USER = Yes and ADMINISTRATION USER = Yes.
Customer Lead User (w/o Administration)	User defined for a Customer with LEAD USER = Yes and ADMINISTRATION USER = No.
Customer Non-Lead User	User defined for a Customer with LEAD USER = No (ADMINISTRATION USER will automatically be No).
Vendor Lead User (w/ Administration)	User defined for a Vendor with LEAD USER = Yes and ADMINISTRATION USER = Yes.
Vendor Lead User (w/o Administration)	User defined for a Vendor with LEAD USER = Yes and ADMINISTRATION USER = No.
Vendor Non-Lead User	User defined for a Vendor with LEAD USER = No (ADMINISTRATION USER will automatically be No).
3rd Party User	User defined for a 3rd Party.
Administrator	User defined as an Administrator.

FIGURE 24

0996710-092801
108260-01/99660

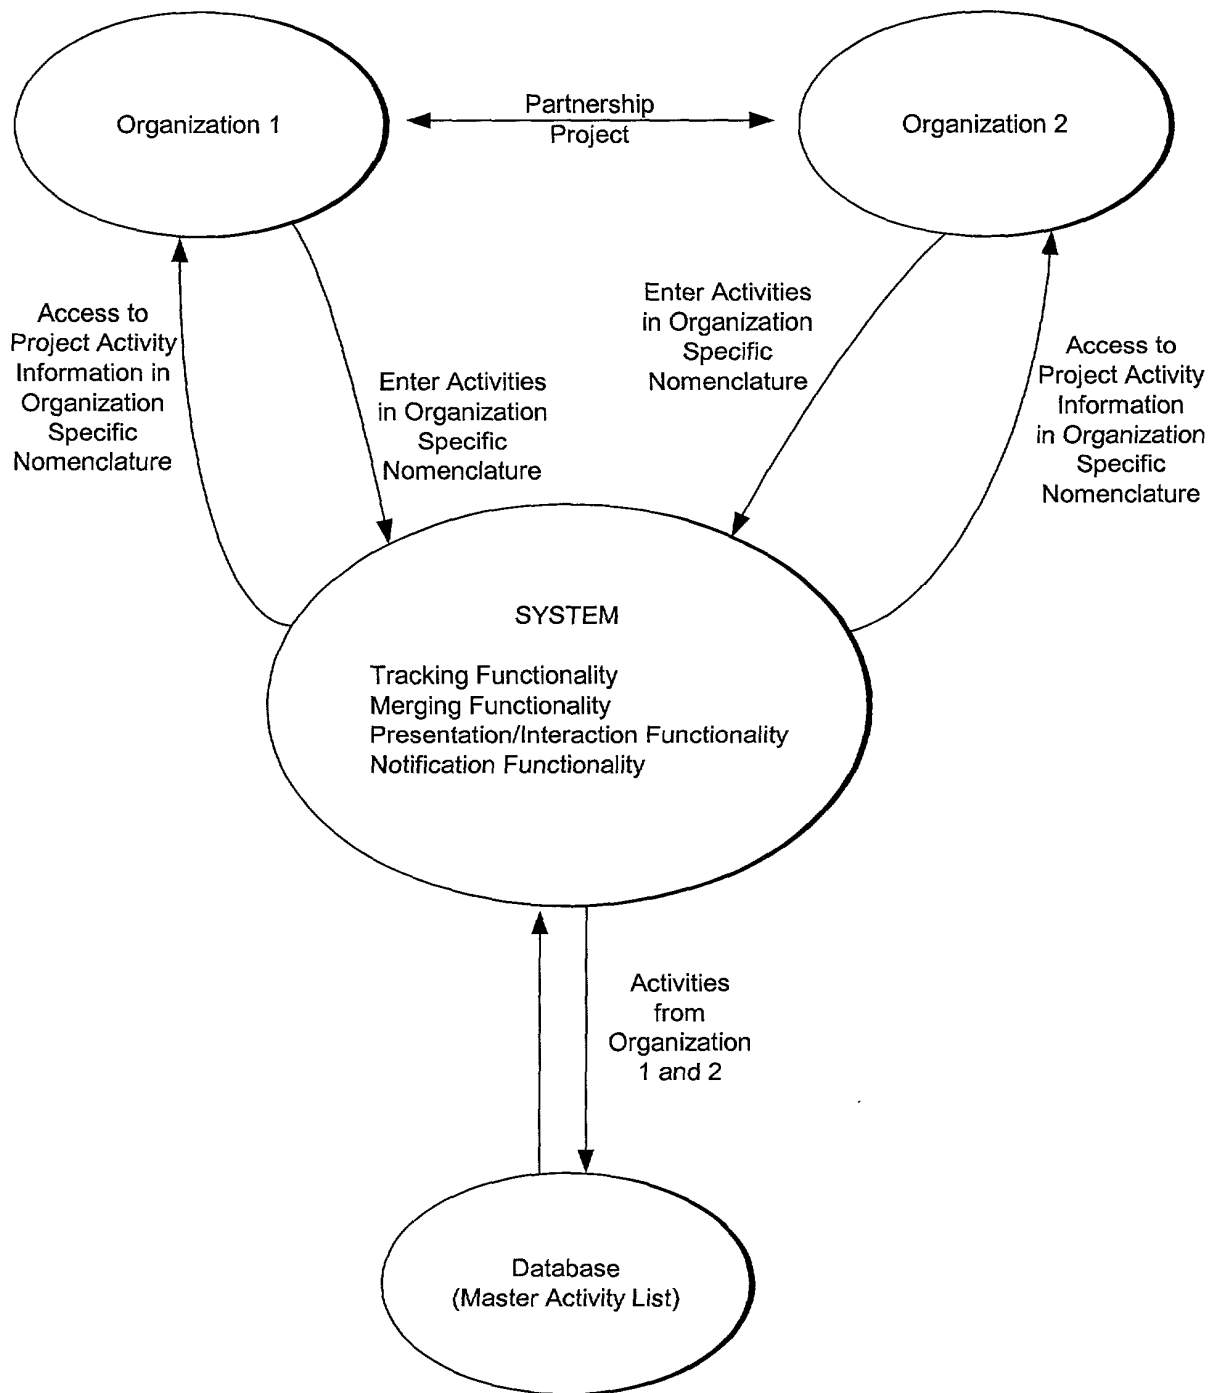


Fig. 25

09966710-092801

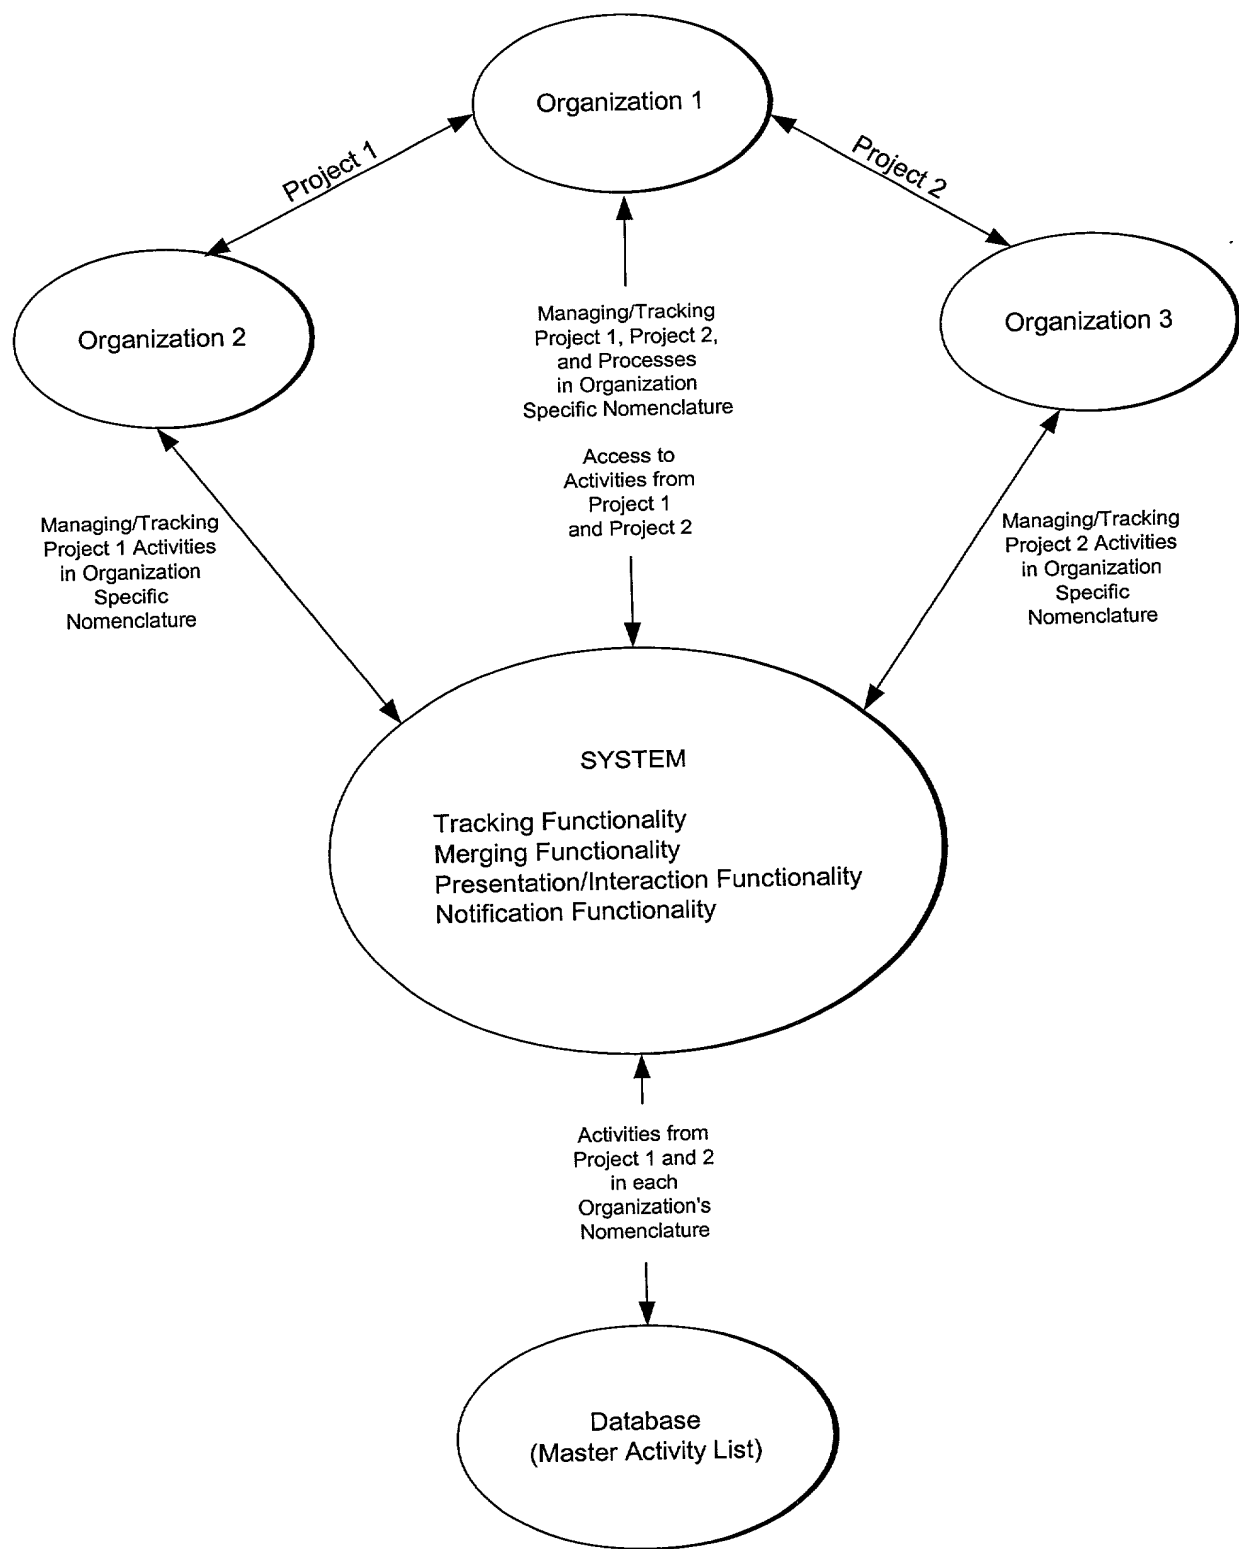


Fig. 26
